

FIG. 1

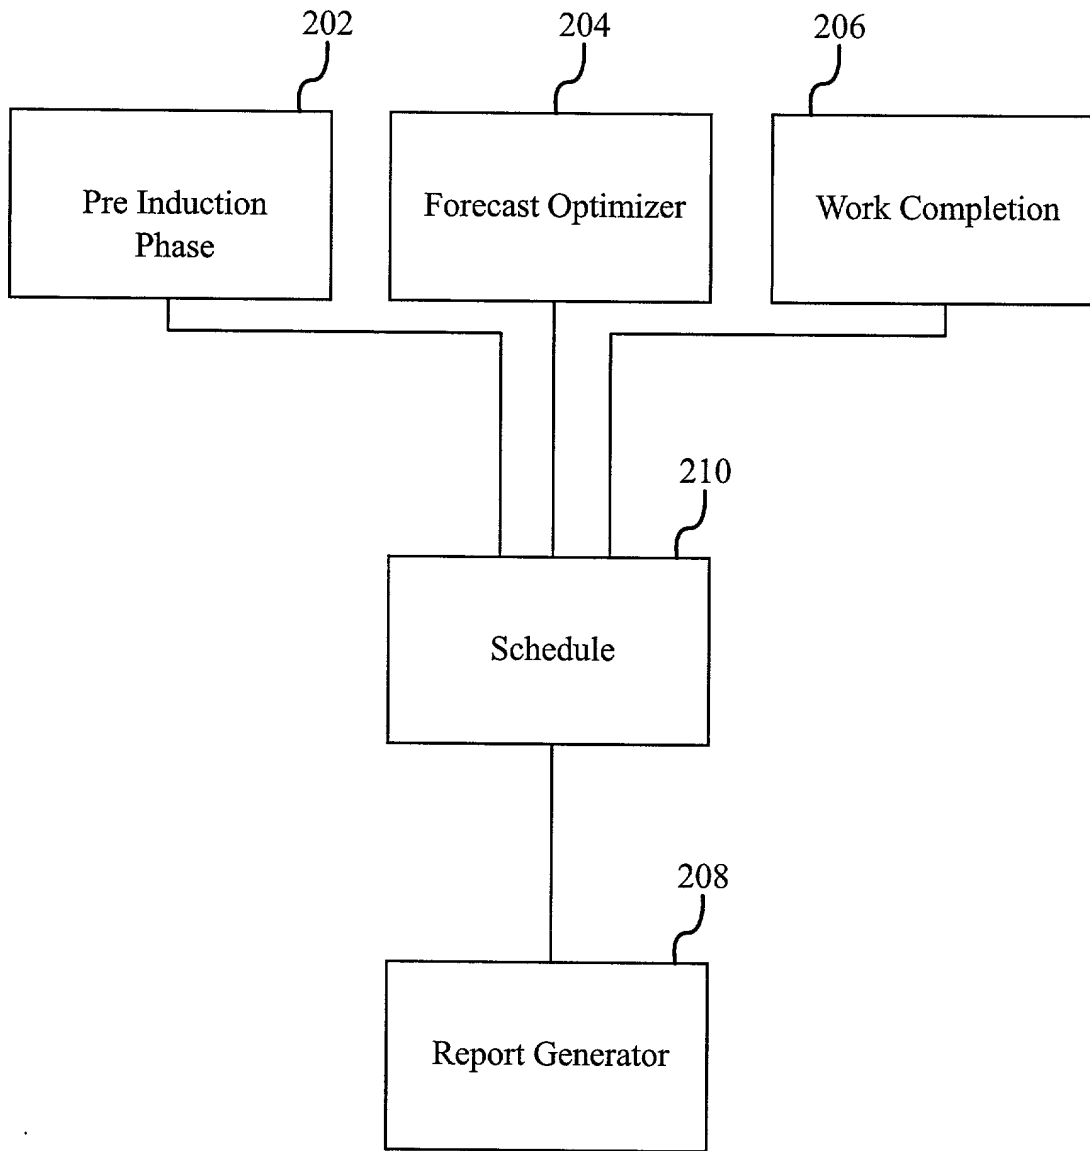


FIG. 2

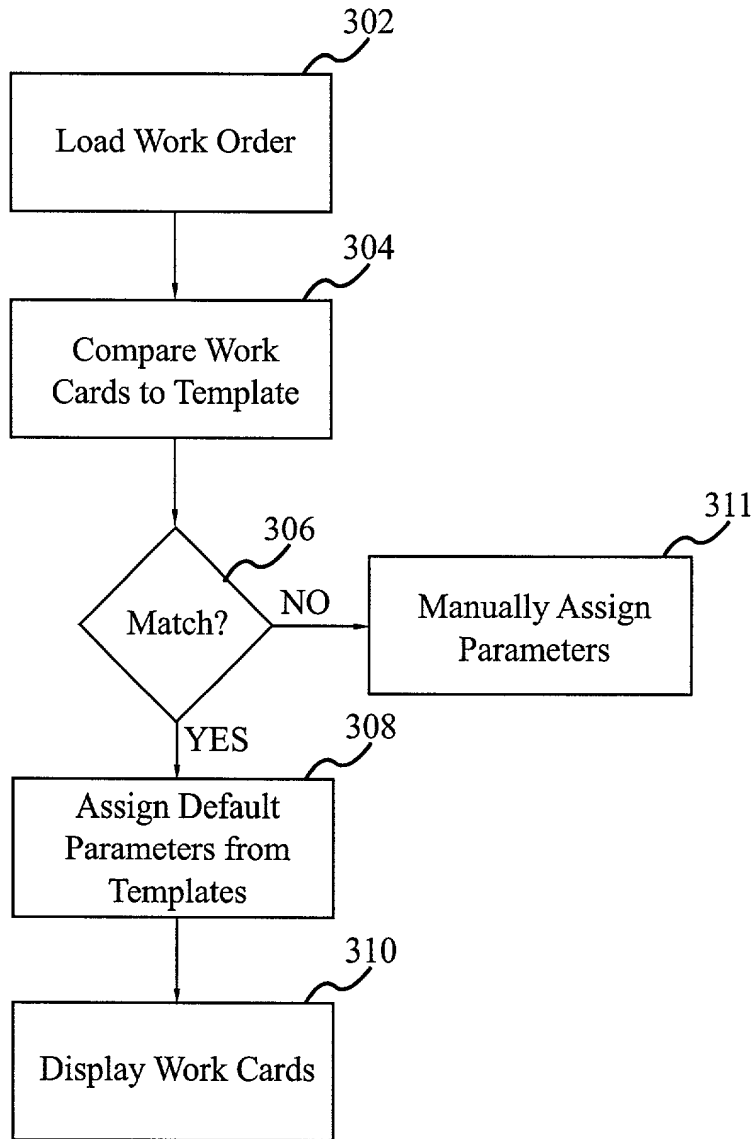


FIG. 3

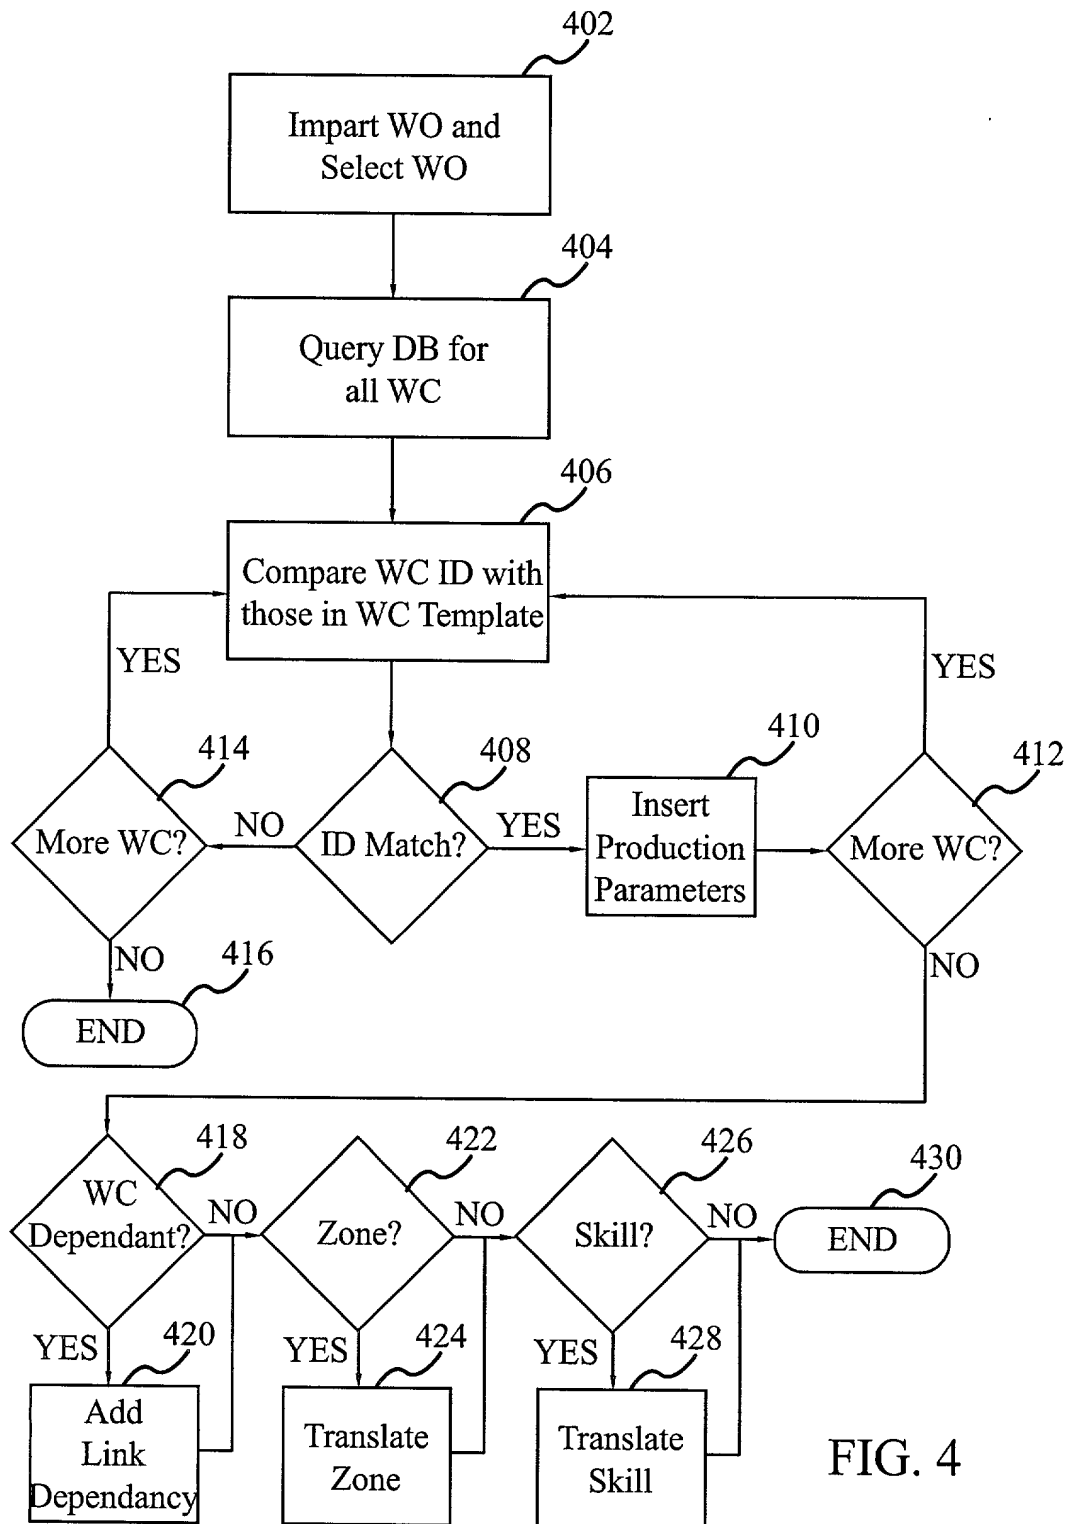


FIG. 4

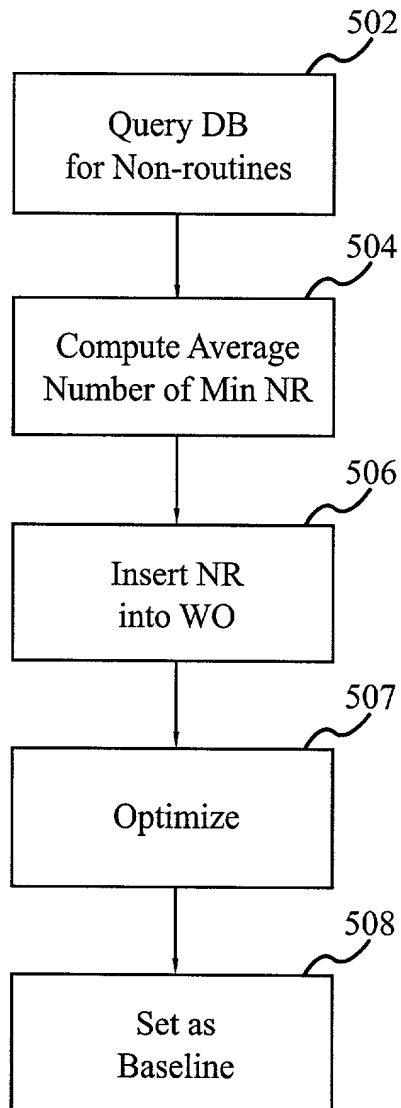


FIG. 5

642

644

624

646

622

648

626

628

630

632

634

636

638

640

602

600

605

606

608

610

612

614

616

617

618

619

604

Check Flow Generator

Check View

Report Designer

WC Template

Work Card Center:

625

Work Order:

11411141 B Check

Aircraft Type:

MD11

Operation Day:

866

Card Set:

All

Open

Close

End

Start Date/Time:

04/14/1999 09:00:00

Tail Number:

N605FE

Total Cards:

97

Date

Location:

MEM

Model Number:

601

Open Cards:

91

Open

Import

Update

NRs

MODs

Suspend

Schedule

RT

Sequence

Sort

Day

<

>

Card

Total Entries

Work Cards:

05-0001

05-0003

05B0001

05B0002

05B0100

05B0201

Day	<	>	Card	Total Entries	Work Cards:
0 1	1	Grave	Cleared	4	05-0001
1 2	8	Day	Open	1	05-0003
2 1	18	Swing	Open	2	05B0001
3 1	7	Swing	Open	3	05B0002
4 1	12	Gave	Open	4	05B0100
5 1	12	Day	Open	1	05B0201
6 1	13	Day	Open	2	
7 3	12	Day	Open	3	
8 1	12	Day	Open	4	
9 1	12	Day	Open	1	
10 1	12	Day	Open	2	

Day	Hour	Shift	Status	Priority	Milestone	Type	Card	Zone	Skill	Manhours	Actuals	Description
0 1	1	Grave	Cleared	4	A02	MP	05-00100	500	0.25	0	A/C Staging	
1 2	8	Day	Open	1	F03	MP	05-00100	500	10.50	0	A/C Staging	
2 1	18	Swing	Open	2	E03	MP	05B00100	200	5.00	0	Aircraft Int	
3 1	7	Swing	Open	3	E03	MP	05B00100	500	4.50	0	Wing Tip S	
4 1	12	Gave	Open	4	C01	MP	05B00100	500	1.00	0	Pre-Dock C	
5 1	12	Day	Open	1	D02	MP	05B00100	500	2.00	0	General Vis	
6 1	13	Day	Open	2	D02	MP	05B00100	500	1.00	0	Hydraulic F	
7 3	12	Day	Open	3	G01	MP	05B00100	500	2.00	0	Post-Dock	
8 1	12	Day	Open	4	D02	MP	05B00100	500	1.00	0	FWD & AF	
9 1	12	Day	Open	1	D02	MP	05B00100	500	4.25	0	Lower Cargo	
10 1	12	Day	Open	2	D02	MP	05B00100	500	0.75	0	Bulk Cargo	

FIG. 6

710

702

706

704

708

Check Flow Generator

PSS View

Report Designer

WC Template

Off

Orig Baseline

Scenario Reference: Orig Baseline

Full Task View

3days

Help

April 14, 1999		April 18, 1999		Tue. April 20	
Wed. April 14	Thu. April 15	Fri. April 16	Sat. April 17	Sun. April 18	Mon. April 19
<p>A/C Staging Predock Functions</p> <p>A/C Staging and Postdock Runs/Functions</p> <p>Aircraft Interior Cleaning AT [B] Check</p> <p>Wing Tip Strobe Light Lenses Clean and Inspect</p> <p>Pre-dock General Open Up</p> <p>General Visual Exterior Inspection</p> <p>Hydraulic Filter Clogging Indicators Check</p> <p>Fwd and Aft Cargo CMPT Drain Sys Ck</p> <p>Lower Cargo Compartments Zonal Inspection</p> <p>Bulk Cargo Compartment Separation NET-DVT</p> <p>Fwd &amp; Aft Cargo CMPT Latches &amp; Guides Ck</p> <p>Post-dock and General Close-up</p>					

Save

Update

FIG. 7

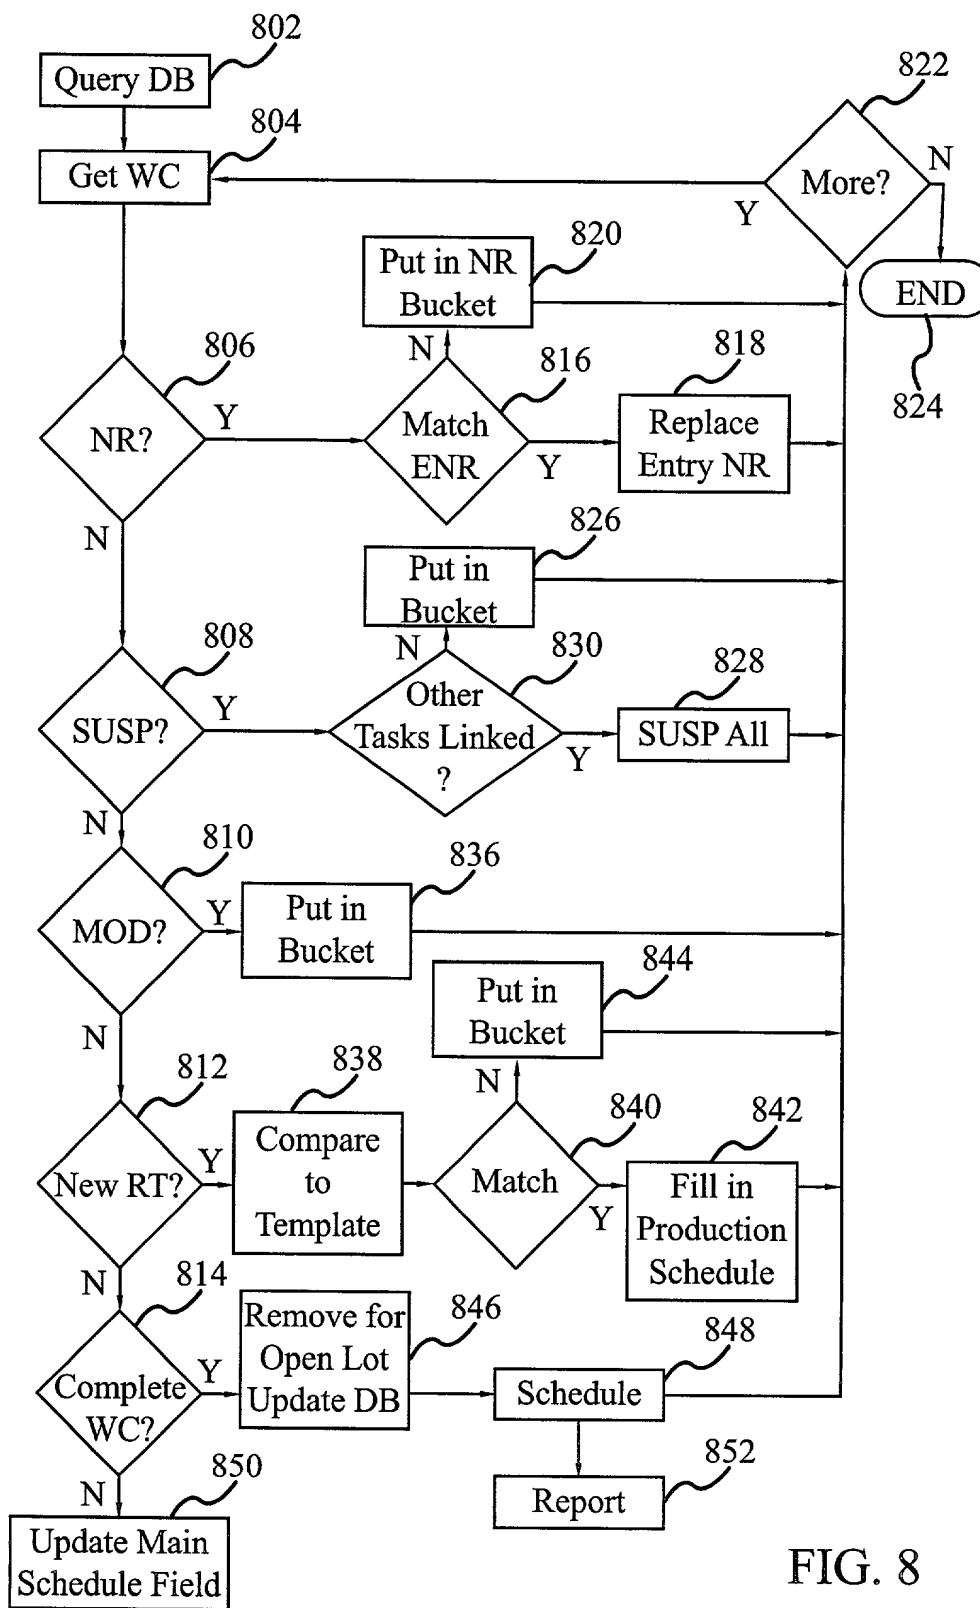


FIG. 8




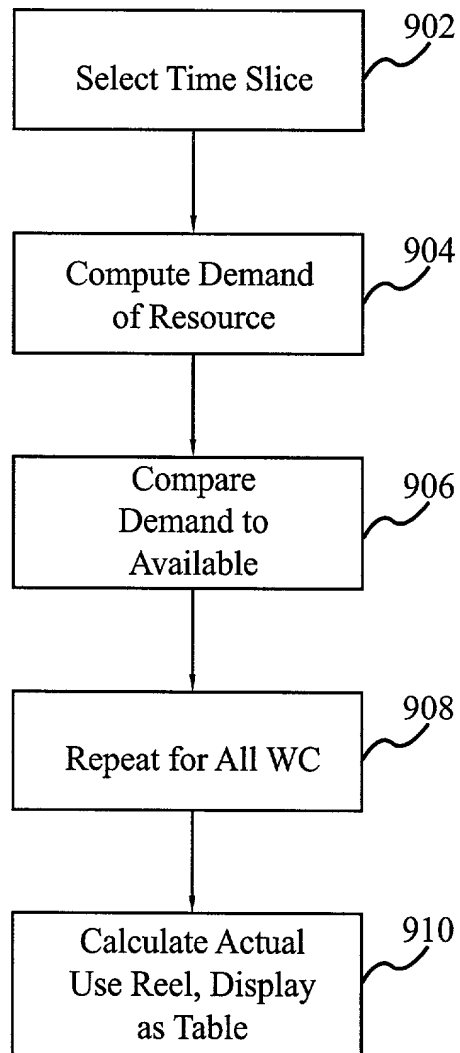


FIG. 9

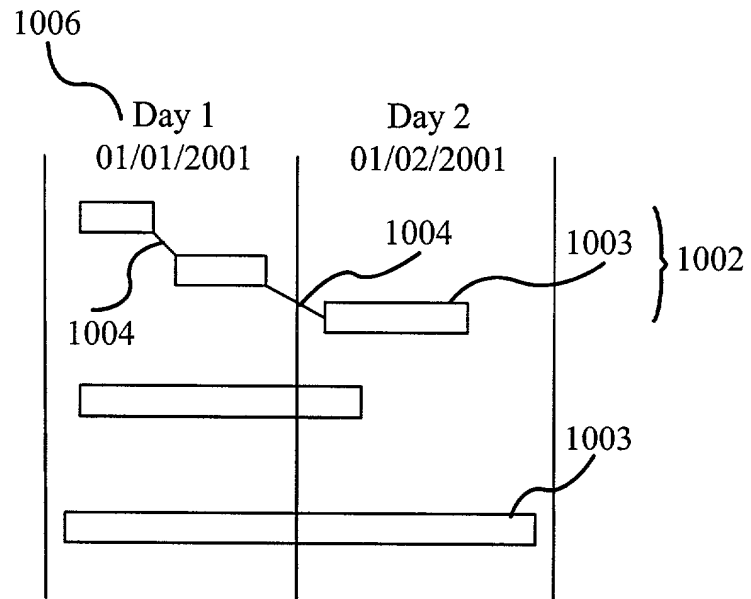

	Demand	Available	Under	Over	} 1010 Resources
01/01/2001	65	40	---	25	
01/02/2001	40	50	10	0	

FIG. 10

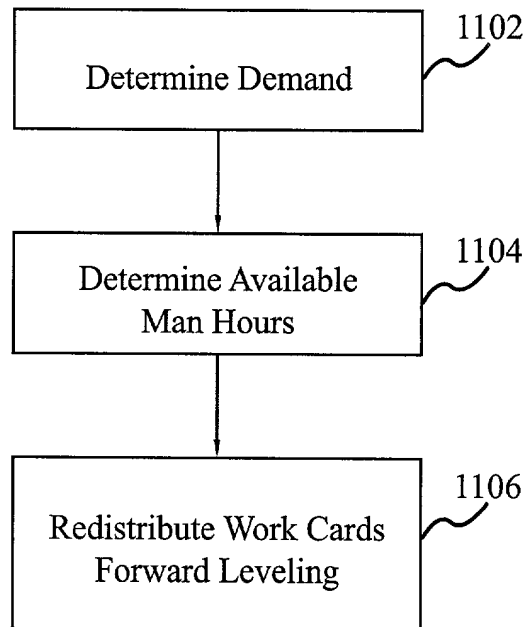


FIG. 11

0937307.091901



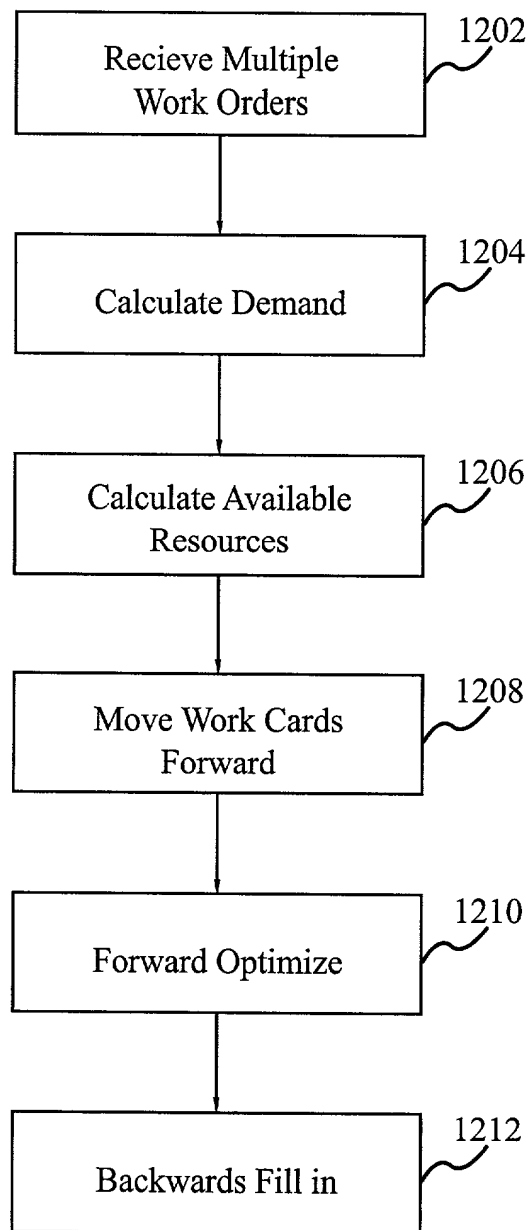


FIG. 12

1308

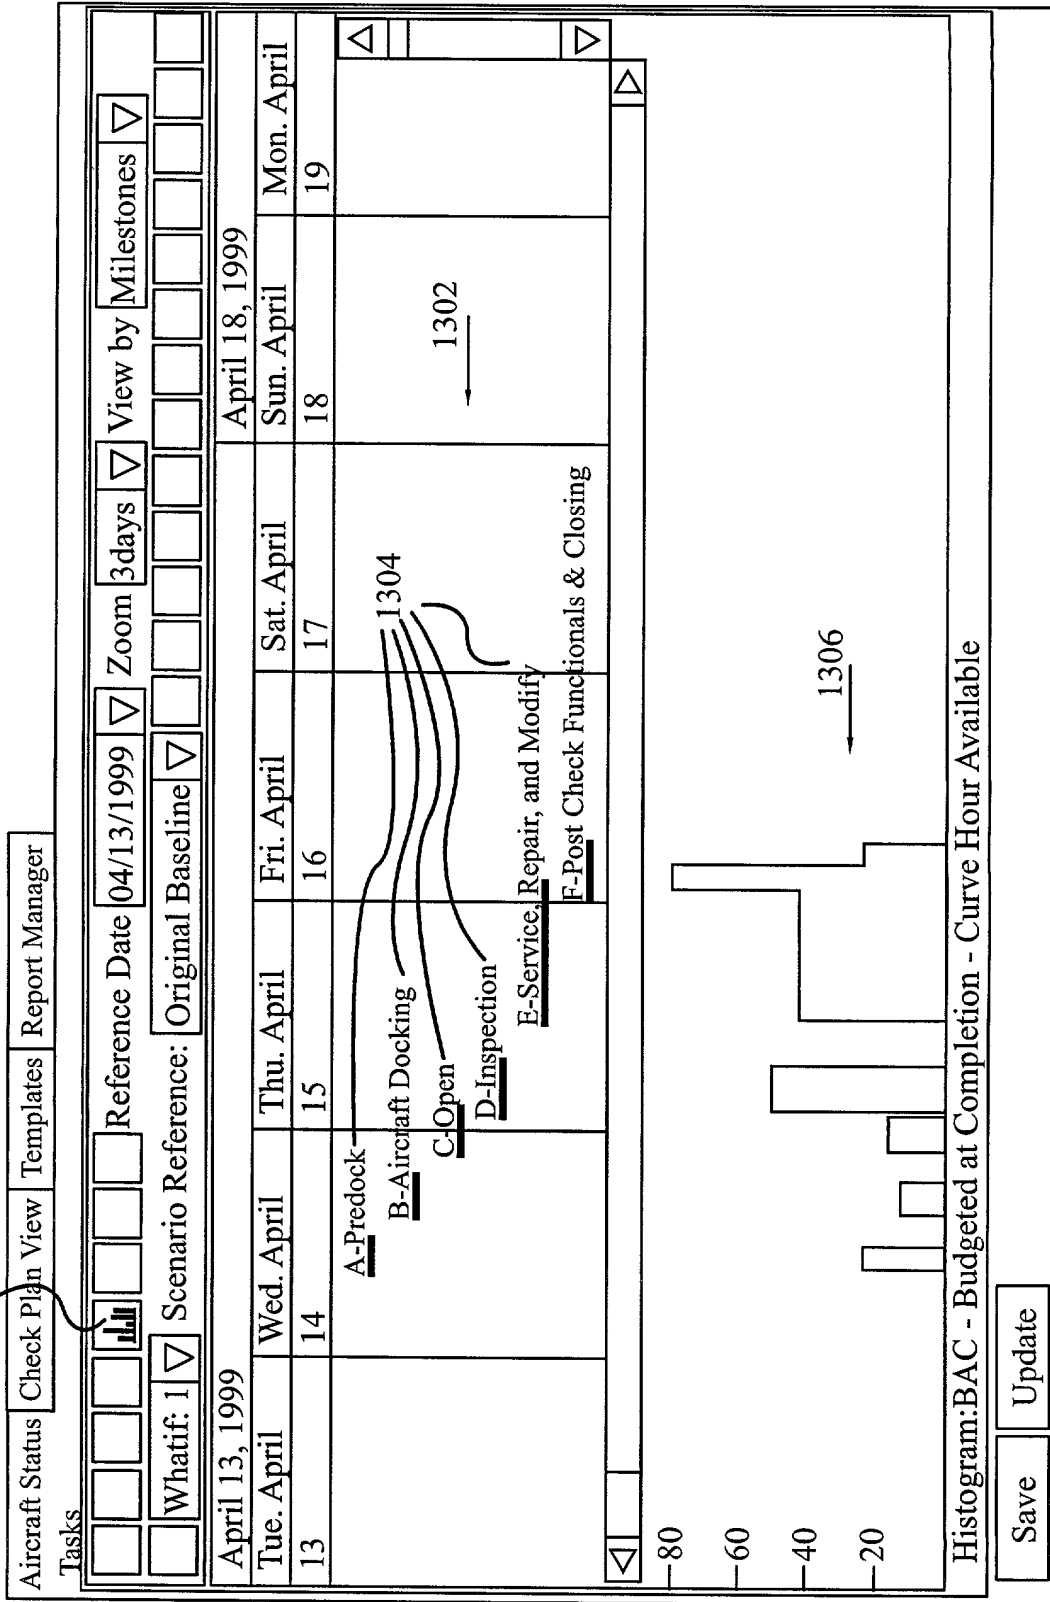


FIG. 13

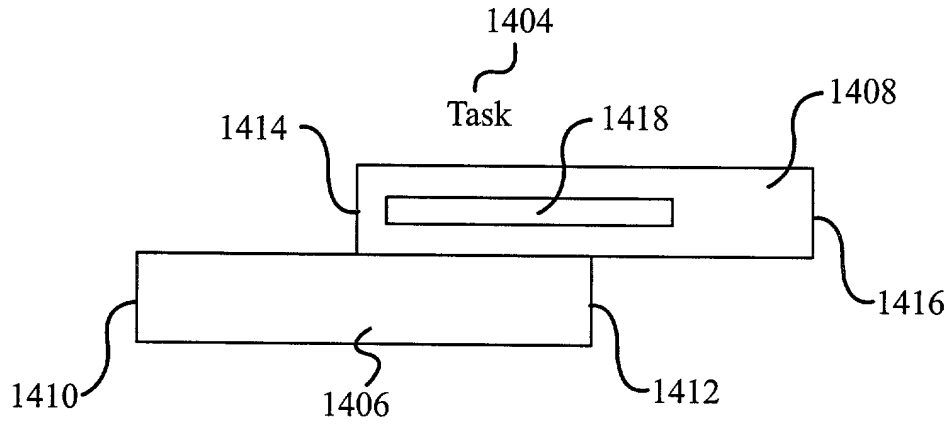


FIG. 14

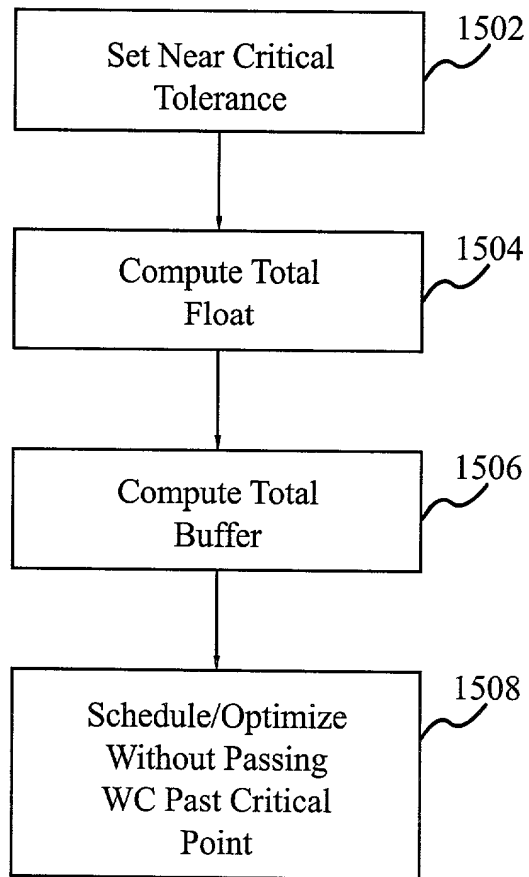


FIG. 15
